


**GMP**  
Total Construction Budget:  
\$204 000 000  
Total Completed To Date:  
\$25 683 593

**Percentage Complete**

15%



**Progress Photos**




Delivery Berth & Heavy Lift Platform 30 inch Steel Pipe Pile

Delivery Berth(Annex) Combiwall 42 inch Steel Pipe Pile With Intergrated Sheet Piles.

Stock Pile of Fill Material for the Central Wharf In-fill Operation

**Pile Driving Delivery Berth**

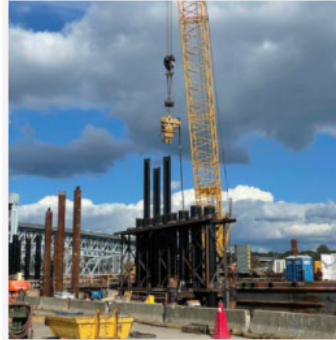


**Schedule Update**

**Percentage Complete**

153 Days Elapsed

Substantial Completion  
Jan 16th 2023  
Final Completion  
April 15th 2023



**5 Key Activities Next 90 Days**

1. Receive Federal Permit
2. Execute Final GMP
3. Complete Mooring Dolphin Demolition
4. Receive Balance of Steel Pipe Piles
5. Commence Infill of Central Wharf Area

**Trade Contractor Progress**

- **Blakeslee at Mooring Dolphins 92% complete**
  - Removing of existing piles to be completed in 2 weeks
- **ECD Activities Delivery Berth**
  - Continued vibrating 30" pile at the Delivery Berth.
  - Total Pipe Piles installed 106
  - PDA testing completed.
  - Obstructions encountered at 30 to 35 feet
- **Kiewit Activities (Annex, Combi Wall, Central Wharf)**
  - Obstruction exploration in the ANNEX ongoing
  - Combiwall template manufactured and delivered
  - Driving of Combiwall commenced 7 pipe piles and 5 sheet piles installed
