
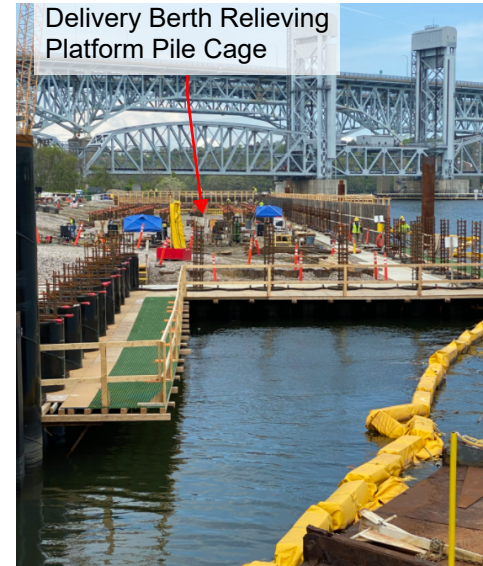


Total Construction Budget:
Target GMP Estimate \$204 000 000

Total Completed To Date:
\$ 86 654 180

Total Expenditure vs Total Approved GMP Contract Value




Schedule Update

Percentage Complete

Substantial Completion*
February 28, 2023

Final Completion*
June 1, 2023



*To be confirmed

Trade Packages Nearing Or At Substantial Completion

1. Steel Pipe Pile Supply Package 100% complete
2. Building Demolition Package 100% complete
3. Mooring Dolphin Demo Package 100% complete
4. Temp Electrical Install Package 100% complete
5. Temp Plumbing Install Package 100% complete
6. Bridge & Retaining Wall Demolition Package 100% complete

*GMP not yet finalized - negotiations ongoing

Progress Photos

