


Total Construction Budget:
\$ 220,000,000

Target GMP Estimate

Total Completed To Date:
\$ 103,701,500

Total Expenditure vs Total Approved GMP Contract Value




Schedule Update

Percentage Complete




Substantial Completion*
February 28, 2023

Final Completion*
June 1, 2023



*To be confirmed

Progress Photos

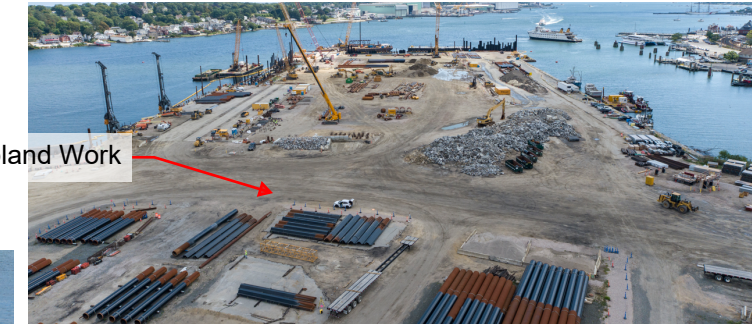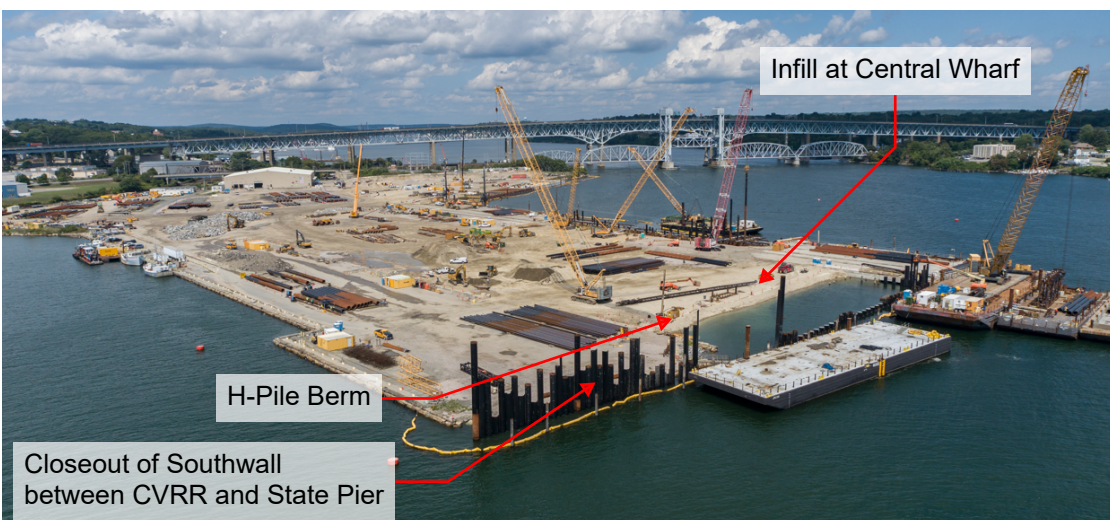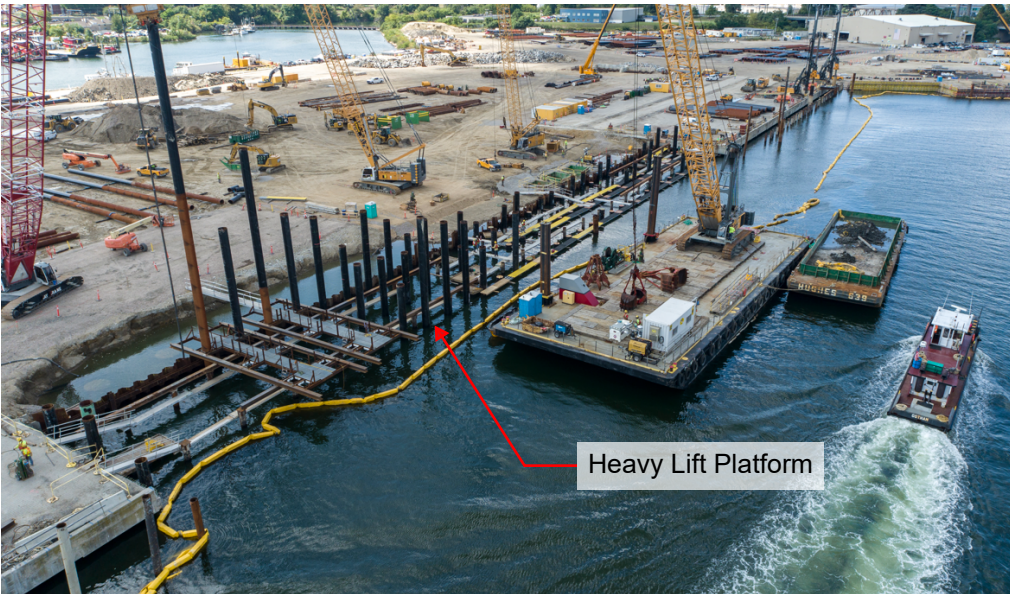

Trade Packages Nearing Or At Substantial Completion

1. Steel Pipe Pile Supply Package 100% complete
2. Building Demolition Package 100% complete
3. Mooring Dolphin Demo Package 100% complete
4. Temp Electrical Install Package 100% complete
5. Temp Plumbing Install Package 100% complete
6. Bridge & Retaining Wall Demolition Package 100% complete
