











CPA Accepted GMP Total Construction Budget:
\$ 274,442,148

Total Completed To Date:
\$ 272,600,000

Total Construction Completed vs. GMP



Progress Photos

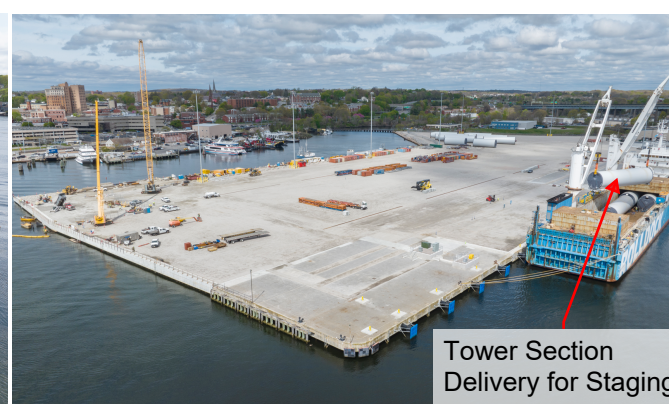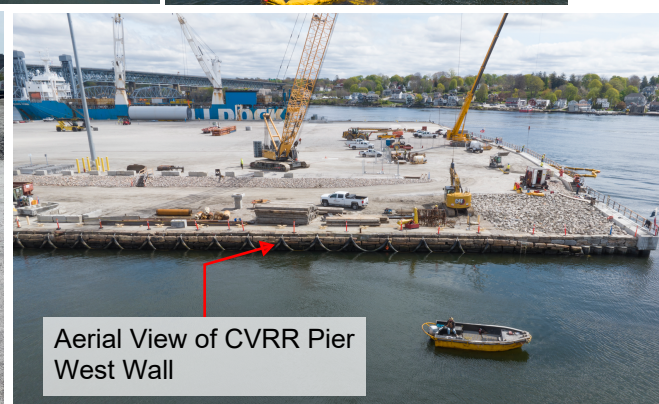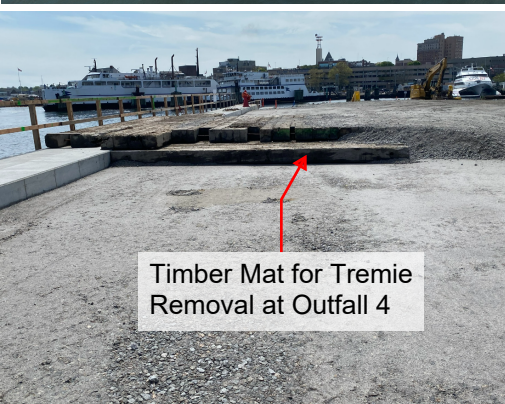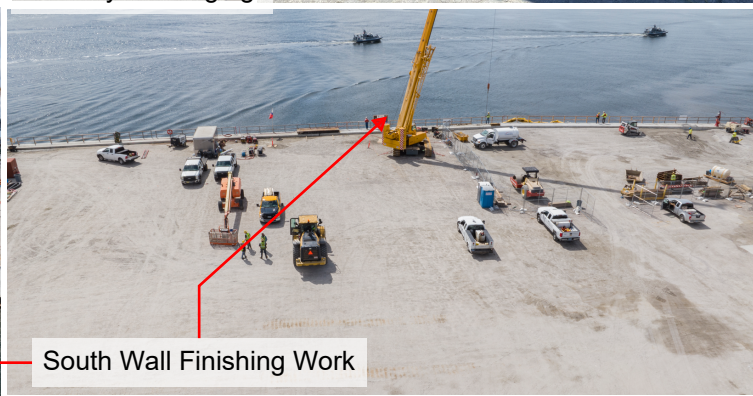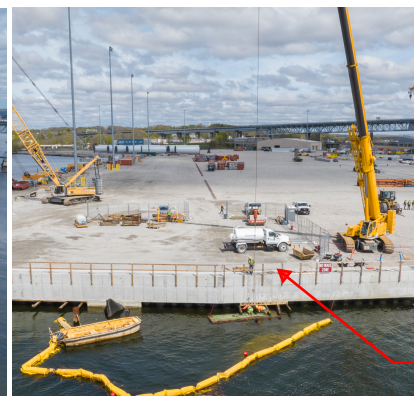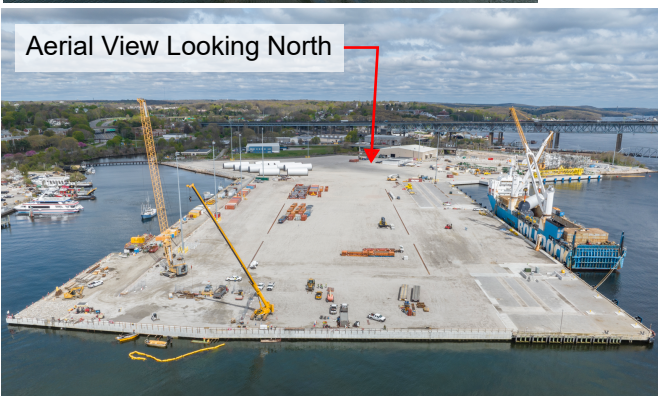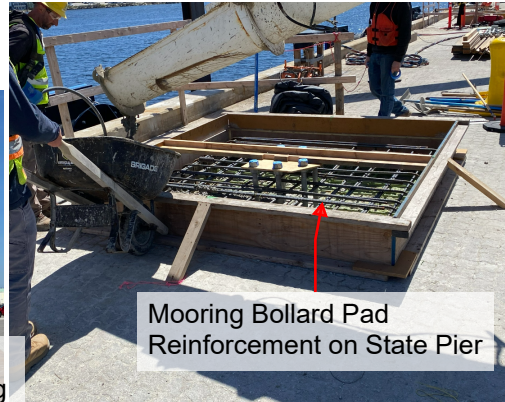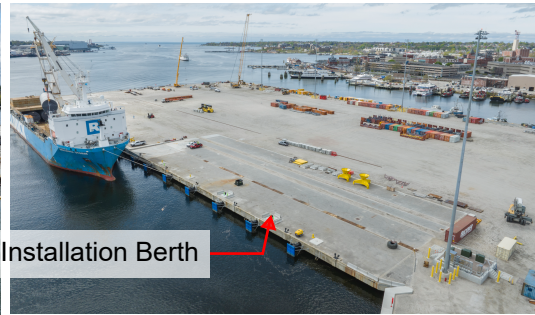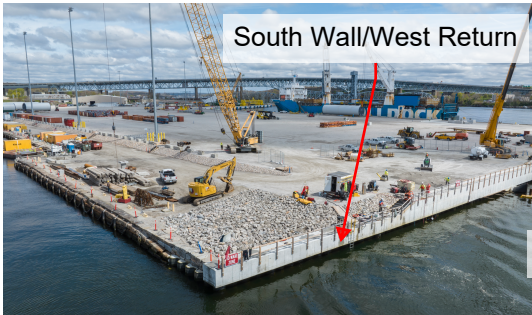

Schedule Update:

| Start Date | Final Acceptance |
|------------|------------------|
| May 2021 | 2nd Qtr 2024 |

*Indicates substantial completion dates have been achieved.
**Indicates partial completion dates have been achieved.

Substantial Completion

(A1*) Feb 28, 2023; (A4.1*) Jul 28, 2023; (A6**) Apr 29, 2024
(A2*) Apr 21, 2023; (A4.2*) Oct 7, 2023; (A7) May 24, 2024
(A3*) Jun 9, 2023; (A5*) Oct 12, 2023

Trade Packages Nearing Or At Substantial Completion

- | | |
|------------------------------------|-----------------------------------|
| 1. Steel Pipe Pile Supply | 11. Drilled Shafts (for HML) |
| 2. Building Demolition | 12. Asphalt Paving |
| 3. Mooring Dolphin Demo | 13. Dredging |
| 4. Temp Electrical Install | 14. Site Civil |
| 5. Temp Plumbing Install | 15. State Pier Relieving Platform |
| 6. Bridge & Wall Demolition | 16. Electrical Demo & Install |
| 7. NE Bulkhead Heavy Lift Platform | 17. High Mast Lights |
| 8. Temp & Permanent Fence | 18. Trackwork |
| 9. Temp Guard Booth | 19. Rebar |
| 10. Water Main & Hydrants | |

