


Total Construction Budget:
Target GMP Estimate \$204 000 000

Total Completed To Date:
\$58 055 574

*GMP not yet finalized - negotiations ongoing

Total Expenditure vs Total Approved GMP Contract Value




Schedule Update

Percentage Complete


Substantial Completion*
January 16, 2023

Final Completion*
April 15, 2023




*To be confirmed



Progress Photos

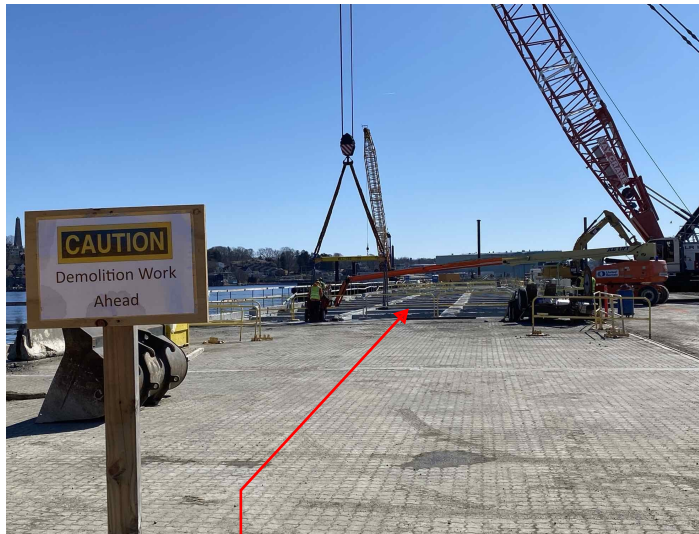

Demolition at East Deck

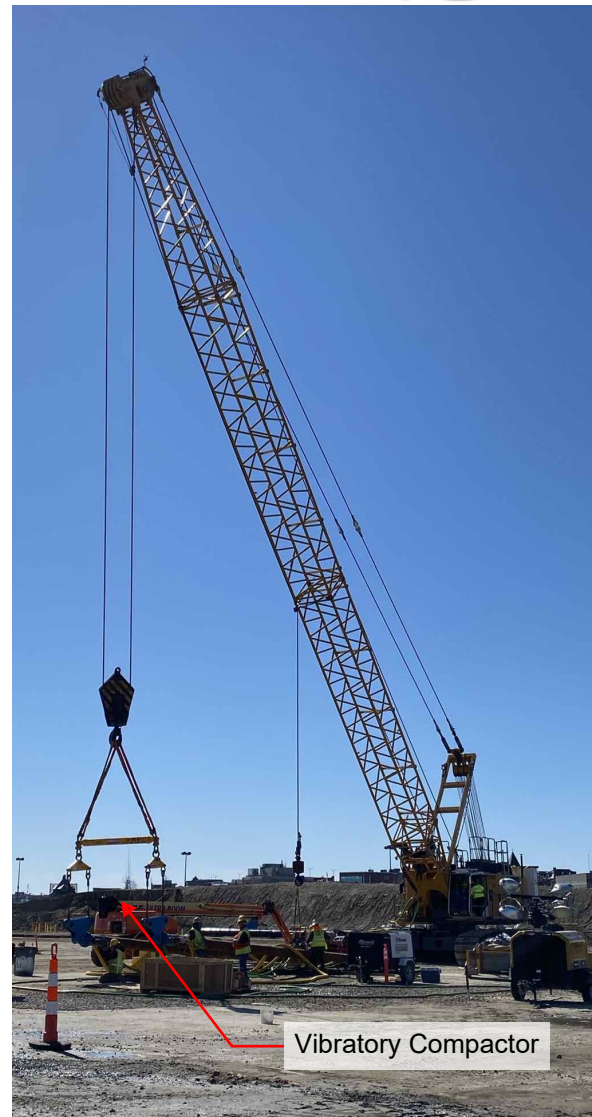

Vibratory Compactor

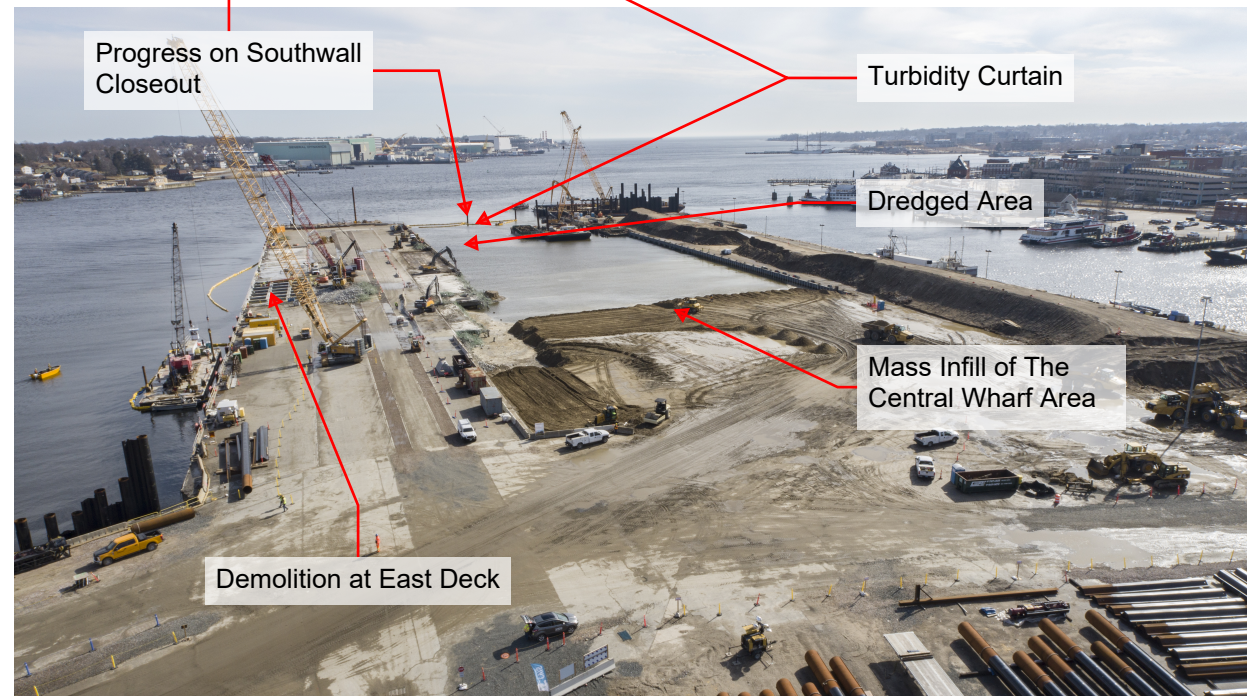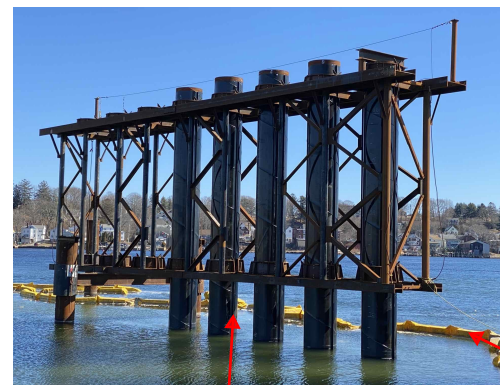

Progress on Southwall Closeout

Turbidity Curtain

Dredged Area

Mass Infill of The Central Wharf Area

Demolition at East Deck

Trade Packages Nearing Or At Substantial Completion

1. Steel Pipe Pile Supply Package 100% complete
2. Building Demolition Package 100% complete
3. Mooring Dolphin Demo Package 100% complete
4. Temp Electrical Install Package 100% complete
5. Temp Plumbing Install Package 100% complete
