


Total Construction Budget:  
Target GMP Estimate \$204 000 000  
  
Total Completed To Date:  
\$ 50 002 207

*\*The Final GMP will be developed once the federal permit has been received*

Total Expenditure vs Total Approved GMP Contract Value



Progress Photos





Turbidity Curtain  
Dredging of organics along S wall

Mogul material placement  
Stockpiled Fill Material



Mass Excavation Site  
42 inch Pipe Pile (King Pile)  
Combiwall Installation  
  
30 inch Pile Installation  
Sample of Combiwall concrete  
and formwork

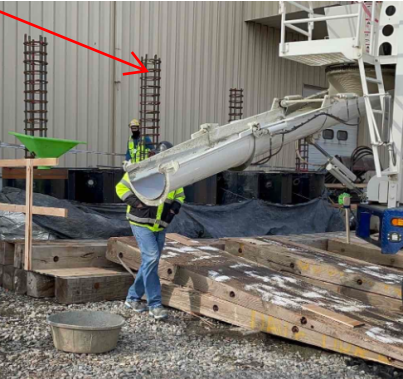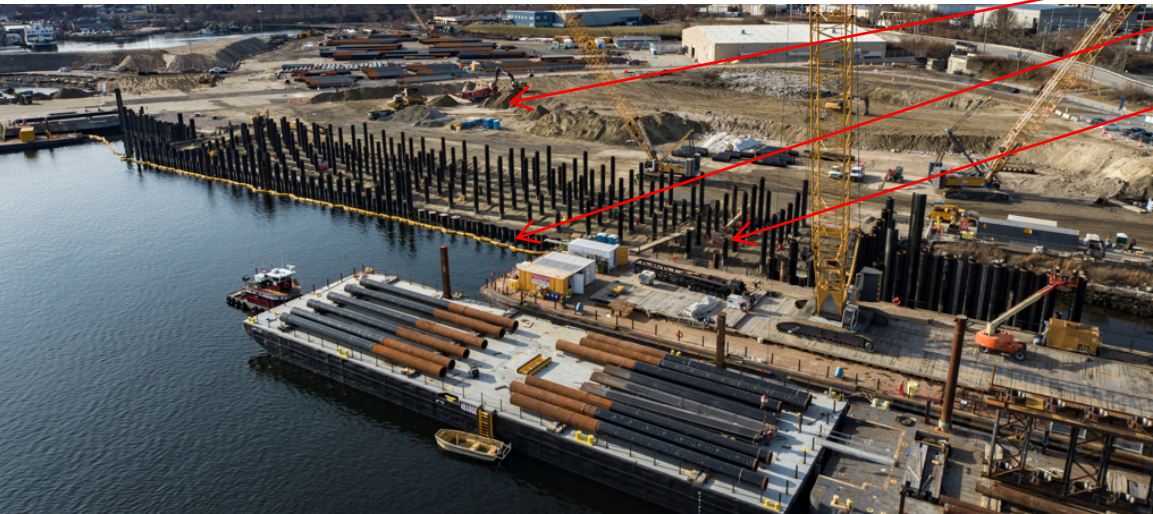

Schedule Update

Percentage Complete

Substantial Completion  
Jan 16th 2023  
Final Completion  
April 15th 2023



Near Term Activities

1. Finalize GMP
2. Infill of the Central Wharf
3. Demolition Portion of the State Pier Deck

Trade Contractor Progress

- **Elevated Deck Demolition**
  1. Started removal of pavers to expose deck
  2. Saw cutting of the concrete deck
- **Dredging**
  1. Dredging of the South wall organics completed
  2. Debris Removal around the CVRR Pier completed
- **Kiewit Activities (Annex Combi Wall Central Wharf)**
  1. Continued install of 42 inch King piles along the NE Bulk head.
  2. Toe Wall piles installed at the NE
  3. Central wharf infill progressing with mogul mound installation prior to mass filling.
  4. Sample of the Combiwall concrete and formwork started.
- **Trade Packages Nearing Or At Substantial Completion**
  1. Steel Pipe Pile Supply Package 100% complete
  2. Building Demolition Package 100% complete
  3. Mooring Dolphin Demo Package 100% complete
  4. Temp Electrical Install Package 100% complete
  5. Temp Plumbing Install Package 100% complete
